HIRA
R.R. ISPAT

File No. RRI/EMS/ 468

Date: 15.11 2021

To,
The Scientist – C,
Ministry of Environment, Forest & Climate Change
Integrated Regional Office, Aranya Bhawan
North Block, Sector-19
Naya Raipur, Atal Nagar,Chhattisgarh- 492002

Subject: Submission of six monthly reports on status of compliance of the conditions stipulated in Environment Clearance.

Reference : Environmental Clearance vide letter No. 834/SEIAA-CG/SIA/CG/IND/468 Naya Raipur dated 19/01/2018.

Dear Sir,

This has reference to the Environment Clearance for our Rolling Mill of capacity 214000 TPA situated at Urla Industrial Area, Raipur, Chhattisgarh.

We are submitting the six monthly compliance status in respect of the above EC for the period from **Apr, 2021 to Sept, 2021**.

This is for your kind information and necessary record please.

Thanking you,

Yours faithfully,
For; **RR Ispat (A Unit of Godawari Power &Ispat Ltd.)**

Authorized Signatory

SIX MONTHLY COMPLIANCE REPORT

PART-I: DATA SHEET

1	Project Type: River-valley/Mining/Industry/Thermal/ Nuclear/Other (Specify)	Industry
2	Name of the project	Rolling Mill Expansion from 1.00 lac TPA to 2.14 lac TPA R.R. Ispat (A Unit Of Godawari Power &Ispat Ltd.)
3	Clearance Letter(s)/OM No. and date	834/SEIAA-CG/SIA/CG/IND/468 Dated : 19/01/2018
4	Location	Urla Industrial Area, Urla
	a. District (s)	Raipur
	b. State (s)	Chhattisgarh
	c. Latitude/ Longitude	21^0 18.95' to 21^0 19.23' N/ 81^0 36.89 to 81^0 36.97 E
5	Address for correspondence	
	a. Address of the Concerned Project Chief Engineer (With Pin Code & Telephone/ Telex/ Fax Numbers)	**Mr. Dinesh Agrawal** Director RR. Ispat (A Unit of Godawari Power &Ispat Ltd.) Hira Arcade, Near Bus Stand, Pandri, Raipur – 492004 (C.G.) TEL. NO. 0771-4082706, 4082707
6	Salient Features	Enclosed in **Annexure-A**
	a. of the project	
	b. of the environmental management plans	
7	Break-up of the project area	
	a. Submergence Area: Forest & Non-Forest	NIL
	b. Other	Leasehold Land : 0.831 ha Freehold Land : 4.517 ha
	c. Total Plot Area	5.348 ha
	d. Built-up Area	2.894 ha
	e. Open Space available (Including Road)	0.69 ha
	f. Green belt area	1.764 ha
8	Break-up of the Project affected population with enumeration of those losing houses/dwelling units only, agricultural land only, Both dwelling units & agricultural land and landless laborers/artisans. a. SC, ST/Adivasis b. Others	Not Applicable
9	Financial Details	
	a. Project cost as originally planned and subsequent revised estimates and the year of price reference	Gross Investment in the enhanced capacity of 2.14 lac TPA is about Rs.40.49Crores. The investment is Rs. 71.15 crores as on 31/03/2021.

Rukapt

	b. Allocations made for environmental management plans with item wise and year-wise breakup.	The capital cost for EMP will be Rs.1.00 crore and recurring cost for EMP per annum will be Rs. 25 Lacs towards pollution control, plantation, rain water harvesting, etc. Air emission control system — 0.4 Cr. Waste Water treatment system — 0.2 Cr. Solid Waste Management — 0.2 Cr. Tree plantation — 0.05 Cr. Monitoring Cell — 0.05 Cr. Rain Water harvesting — 0.1 Cr. **Total — 1.0 Cr.**
	c. Benefit cost ratio/ Internal Rate of Return and the year of assessment	-
	d. Whether c, includes the cost of environmental management as shown in the above	-
	e. Actual expenditure incurred on the project so far	Rs.71.15 Crores as on 31/03/2021
	f. Actual expenditure incurred on the environmental management plan so far	Rs. 2.42 Crores (Upto September, 2021)
10	Forest land requirement	Not Applicable
	a. The status of approval for diversion of forest land for non-forestry use.	
	b. The status of clearing felling.	
	c. The status of compensatory afforestation, if any	
11	The status of clear felling in non-forest areas (such as submergence area of reservoir, approach roads), if any with quantitative information required.	Not Applicable
12	Status of construction (Actual &/or Planned)	
	a. Date of commencement (Actual &/or Planned)	The commissioning of expanded capacity of 2,14,000 TPA was 21/03/2018.
	b. Date of Completion (Actual &/ or Planned)	
13	Reasons for the delay if the project	Not Applicable.

Rishaad

	is yet to start.	
14	Dates of site visits a) The dates on which the project was monitored by Regional Office on previous occasions, if any	15/05/2015 – Visit of RO, MoEF, Bhopal 30/06/2017 – Visit of RO, MoEF, Nagpur 31/01/2019 – Visit of RO, MoEF, Nagpur
	b) Date of site visit for this monitoring Report.	-
15	Details of correspondence with project authorities for obtaining action plans/ information on status of compliance to safeguards other than the routine letters for logistic support for site visits.	Given as below:

Date	Letter from RO	Date / RR ISPAT Letter date	Reply from PA
28/10/14	Status and compliance called	03/12/14	Point-wise status and compliance submitted
13/08/15	Certified compliance report issued	12/12/15	Compliance status submitted.
-	-	14/06/16	Compliance status submitted
07/07/17	Status Report on the stipulated compliance conditions issued	26/12/16	Compliance status submitted
-	-	06/06/17	Compliance status submitted
-	-	06/06/17	Compliance status submitted
-	-	15/07/17	Clarifications submitted on expansion programme.
-	-	23/12/17	Compliance status submitted
-	-	16/06/18	Compliance status submitted
-	-	24/12/18	Compliance status submitted
-	-	31/05/19	Compliance status submitted
-	-	03/12/19	Compliance status submitted
-	-	18/06/20	Compliance status submitted
		07/12/20	Compliance status submitted
-	-	16/06/21	Compliance status submitted

PART-II

POINT WISE COMPLIANCE STATUS

विषय :–प्लॉट नं 490/1,273/3,273/6,476/2,484, 485,486,490/2,474,489/1 496,497,239/1 239/2, 240, 241, 236/1, 236/2,327/1, 327/2, 327/3,328/1, 328/2,330/1,330/2,324/1,271/5, एंव 271/5 ग्राम –उरला तहसील व जिला–रायपुर में कुलभुमि 7,899 हेक्टयर में रोलिंग मिल 1,00,000 टन/वर्ष से 2,14,000 टन/वर्ष हेतु पर्यावरण स्वीकृति जारी करने के सम्बन्ध में।

REFERENCE : Environmental Clearance vide letter No. 834/SEIAA- CG/SIA/CG/IND/468 Naya Raipur dated 19/01/2018.

S. NO.	EC CONDITIONS	COMPLIANCE STATUS
1	No additional land shall be acquired for expansion project.	Agreed, No additional land has been acquired for expansion project.
2	No furnace oil, LDO, HSD etc. liquid fuel shall be used in the re-heating furnace of rolling mill. Only gas generated from coal gasifier shall be used as fuel in the re-heating furnace of rolling mill.	Agreed, only gas generated from coal gasifier is being used as fuel in the re-heating furnace of rolling mill.
3	Project authority shall provide adequate facility for proper treatment of industrial effluent and domestic effluent. Closed cycle cooling system shall be provided. Minimum water for makeup purposes shall be ensured. Cooling water shall be cooled in cooling system and after cooling reused for cooling purpose. Domestic effluent shall be treated in well-designed septic tank and soak pits. In case of any failure of effluent treatment arrangement, it shall be immediately rectified or same alternate arrangement shall be provided. Treated effluent shall be utilized either in process or for plantation purposes within plant premises. Any liquid effluent what so ever generated from industrial activities and un-treated / treated domestic effluent shall not be discharged into the river or any surface water bodies under any circumstances. The treated domestic effluent shall be used for plantation purpose after proper disinfection. Project authority shall make arrangement of suitable drains / pipe networks to ensure adequate flow	The entire water cycle in the process is in closed circuit, only as per the requirement make up water is being feeded. There is no generation of waste water in the process of rolling mill due to closed circuit. The domestic effluent is being treated in septic tank via soak pit. The company has also established a sewage treatment plant (STP) of capacity 100 KLD for treatment of domestic waste water and after treatment treated water is being utilized for green belt development. The ZLD is being maintained except monsoon periods. Proper drainage arrangement has been provided for diversion of storm water. The treated effluent quality is within standard prescribed by Ministry of Environment, Forest and Climate Change, Government of India. The analysis report is being submitted regularly to RO, CECB, Raipur.

	for full utilization of treated effluent inside the premises. The concept of zero discharge shall be maintained all the time except during monsoon. Arrangements shall be made that effluents and storm water do not get mixed. Project authority shall ensure the treated effluent quality within standard prescribed by Ministry of Environment, Forest and Climate Change, Government of India. Industrial wastewater shall conform to the standards prescribed under GSR 422 (E) dated 19th May, 1993 and December, 1993 or as amended form time to time.	
4	Project authority shall provide adequate measuring arrangements for the measurement of water utilized in different categories and effluent generated before commissioning of the plant with expanded capacity.	Water meters have already been provided for the measurement of water being utilized and the same are operational.
5	Project authority shall ensure that particulate matter emission shall not exceed 40 mg / Nm3 under any circumstances by up-gradation / modification of existing air pollution control systems.	The high efficiency wet scrubber has already been installed to control the particulate matter emission within prescribed standard. The stack emission monitoring is being carried out by adopting isokinetic sampling regularly and report submitted to RO, CECB, Raipur. In addition to this, online continuous monitoring system for continuous measurement of particulate matter has been installed, the real time monitoring data is being uploaded in CECB server.
6	Project authority shall provide adequate air pollution control arrangements at all point and non point sources. Scrubber and air recuperator of adequate capacity and high efficiency shall be installed in rolling mill reheating furnace to ensure outlet dust (particulate matter) emission less than 40 mg / Nm3 all the time. Low NOx burners shall be installed in furnace of rolling mill. Project authority shall install suitable & effective air pollution control equipments at all transfer points, junction points etc. also. All the	The present stack height of rolling mill attached to reheating furnace is 44 meters. Scrubber with ID fan of capacity 15000 m^3/hr for flue gas treatment has been installed between the recuperator and chimney to achieve the outlet dust emission less than 40 mg/Nm^3. The stack emission monitoring is being carried out by adopting isokinetic sampling regularly and report submitted to RO, CECB,

	conveying system, transfer point, junction point etc. shall be covered. Adequate and effective arrangement shall be made for sprinkling of water at strategic locations to ensure dust does not get air borne. For controlling fugitive dust, regular sprinkling of water in vulnerable areas of the plant and internal roads shall be ensured. Proper ventilation shall also be provided in rolling mill plant. The emission of pollutants from any point source shall not exceed the following limit: - Particulate Matter: 40 mg/Nm3 (Forty Milligram per Normal Cu Meter) The Chhattisgarh Environment Conservation Board may specify more stringent standards for the relevant parameters keeping in view the nature of the industry and its size and location. At no time the emission level shall go beyond the prescribed standards. Interlocking facilities shall be provided so that process can be automatically stopped in case emission level exceeds the limit. Project authority shall provide proper space provision for further retrofitting of air pollution control systems in case of further stringency of particulate matter emission limit.Height of the stack attached to reheating furnace of rolling mill shall not be less than 44 meters.	Raipur. In addition to this, online continuous monitoring system for continuous measurement of particulate matter has been installed, the real time monitoring data is being uploaded in CECB server. Water sprinkling facilities have been provided through water tankers at internal roads, Coal Yard etc. to control fugitive emission. Low NOx burners has been installed in furnace of rolling mill. Space provision exists for further retrofitting of air pollution control systems in case of further stringency of particulate matter emission limit.
7	Secondary fugitive emissions shall be controlled and shall be kept within the prescribed limits and regularly monitored. Guidelines / Code of Practice issued by the CPCB in this regard shall be followed. Project authority shall maintain fugitive dust emissions to the minimum level in the areas of road transportation routs of raw material, product to ensure National Ambient Air Quality Standards prescribed including black topping / asphalting / concreting and maintenance with requisite water sprinkling arrangements.	Secondary fugitive emission has been controlled with the following measures : a. All the internal roads and raw material handling yards have been concreted. b. Collection of road spillage materials at regular intervals. c. Regular water sprinkling at dust generating points. d. Proper housekeeping is being maintained. The fugitive emission monitoring is being carried out regularly and the results of the same are within the permissible limits.

		Ambient Air Quality Monitoring Stations (04 Nos) have been established in the plant for the measurement of PM_{10}, $PM_{2.5}$, SO_2& NOx. The Ambient Air Quality Monitoring is being carried out regularly and report submitted to RO, CECB, Raipur.
8	All air pollution control systems shall be kept in good running conditions all the time and failure (if any), shall be immediately rectified without delay otherwise similar alternate arrangement shall be made. In the event of any failure of any pollution control system adopted by the Project authority, the respective production unit shall not be restarted until the control measures are rectified to achieve the desired efficiency.	All air pollution control systems are kept healthy and operational in good condition all the time.
9	Online Continuous Stack Emission Monitoring System shall be installed for measurement of particulate matter. Project authority shall ensure regular transfer of data of Online Continuous Stack Emission Monitoring System to CECB. Regular monitoring of ground level concentration of SO2, NOx, PM10 and PM2.5 at at-least four stations shall be carried out in the impact zone and records maintained. The location of the monitoring stations and frequency of monitoring shall be decided in consultation with Chhattisgarh Environment Conservation Board Raipur. The data so collected shall be properly analyzed and periodic reports shall be submitted to Chhattisgarh Environment Conservation Board, Raipur, Regional Office, Chhattisgarh Environment Conservation Board, Raipur, SEIAA, Chhattisgarh and Regional Office, Ministry of Environment, Forest and Climate Change, Government of India, Nagpur.	Online continuous monitoring system for continuous measurement of particulate matter has been installed, the real time monitoring data is being uploaded in CECB server. Ambient Air Quality Monitoring Stations (04 Nos) have been established in the plant for the measurement of PM_{10}, $PM_{2.5}$, SO_2& NOx. The Ambient Air Quality Monitoring is being carried out regularly and report submitted to RO, CECB, Raipur.
10	Project authority shall install separate electric metering arrangements with time totalizer and interlocking arrangement for the running of pollution control devices. These arrangements shall be made in such a fashion that any non-	We have already installed separate electric meter with time totalizer to monitor energy consumption of the pollution control equipment, record of the same is being maintained properly.

	functioning of pollution control device / devices shall immediately stop the electric supply to the fuel / raw materials supply system and shall remain tripped till the pollution control device / devices are made functional again / rectified to achieve the desired efficiency.	The procedure is observed regularly that electric supply is being stopped in the case of non-functioning of pollution control equipments.
11	Project authority shall utilize the fly ash bricks / blocks etc. in all construction activities.	Fly ash bricks/blocks, fly ash based products are being used in construction/ repairing activities.
12	Project authority shall take effective steps for safe disposal of solid wastes and sludge. End cutting from rolling mill shall be used as raw material in induction furnace units. Mill scales shall be sold to sinter plant/ Ferro alloys / Casting units. Oily sludge shall be sold to authorized recyclers / re-processors for proper disposal through incineration. Project authority shall obtain authorization from Board for management and handling of hazardous materials as per Hazardous and Other Wastes (Management and Transboundary Movement) Rules, 2016.	End cutting of rolling mill is being reprocessed in in-house units of the plant. Presently 100% heating of raw material has been done by producer gas, hence no oily sludge is generating. Authorization under Hazardous and Other Wastes (Management & Transboundary Movement) Rules, 2016 obtained vide authorization no. 398/HO/HSMD/CECB/Naya Raipur from Chhattisgarh Environment Conservation Board, Raipur (C.G.).
13	Coal ash from coal gasifier shall be used in fly ash brick plant / land filling and coal tar shall be sold to registered vendors. Mill scales shall be collected through sedimentation pit and utilized as a raw material in steel / ferro alloys plants.	The coal ash generated from the coal gasifier is being utilized in the fly ash brick plant/ land filling and coal Tar is being sold to registered vendors. Mill scale is being reprocessed in in-house steel/ferro alloy plants.
14	All the internal roads shall be made pucca. Regular cleaning of roads shall be ensured. Project authority shall adopt good house keeping practices within premises.	All the internal roads are already concreted and good housekeeping is in practices..
15	Project authority shall take proper action to control the noise pollution. Project authority shall install appropriate noise barriers / control measures including acoustic hoods, silencers, enclosures etc. on all sources of noise generation to control the noise. Earplugs / ear muffs etc. shall be provided to the employee working in the high noise areas. Leq of / noise levels emanating from machines shall be limited to 75 dB (A). The noise level shall not exceed the limits 75 dB (A) during the daytime and 70 dB	Control measures such as maintenance of all machines are being done regularly. The noise level is well within prescribed standard in the plant premises as well as work environment. However, as a precaution, the workers engaged at noisy areas are being providing with ear plugs/muffs. Workmen (15 Nos) engaged in noisy areas has been examined in year 2021 and audiometric

	(A) during the night time within the factory premises. Project authority shall take adequate measures for control of noise level below 85 dB (A) in the work environment. Workers engaged in noisy areas shall be periodically examined to maintain audiometric record and for treatment for any hearing loss including rotating them to non-noisy / less noisy areas.	test report is enclosed as **Annexure –I.**
16	First aid and sanitation arrangements shall be made for the drivers and other contract workers.	First aid and sanitation arrangement is available for drivers and other contract workers.
17	Up-gradation / modification of effluent treatment system and air pollution control equipments shall be taken up simultaneously with other civil / mechanical works of expansion (if any). The progress of the activities related to the project shall be submitted periodically to Chhattisgarh Environment Conservation Board, Raipur, Regional Office, Chhattisgarh Environment Conservation Board, Raipur, SEIAA, Chhattisgarh and Regional Office, Ministry of Environment, Forest and Climate Change, Government of India, Nagpur.	The capacity of existing effluent treatment system and air pollution control equipments is sufficient to achieve the prescribed norms (waste water & air).
18	Adequate safety measures shall be provided in the plant area to check / minimize spontaneous fires. Copy of the these measures with full details along with location plant layout shall be submitted to Chhattisgarh Environment Conservation Board, Raipur, Regional Office, Chhattisgarh Environment Conservation Board, Raipur, SEIAA, Chhattisgarh and Regional Office, Ministry of Environment, Forest and Climate Change, Government of India, Nagpur.	Spontaneous fires prone areas have already been equipped with different category of fire extinguishers to check/ minimize spontaneous fires.
19	Disaster Management plan shall be prepared to meet any eventuality in case of an accident taking place. Mock drills shall be conducted regularly and based on the same, modifications required, if any shall be incorporated in the DMP.	Disaster Management plan has been prepared and to be submitted to Health & Safety Department.
20	As far as possible maximum area of open spaces shall be utilized for plantation purposes. Project authority shall abide by the decisions taken by Ministry of Environment, Forest and Climate	Agreed, adequate wide green belt of Local broad leaf species has been developed in the 1.764 ha land (Copy plantation report is enclosed as **Annexure -II).**

	Change, Government of India / Central Government / Central Pollution Control Board from time to time in this regard. Adequate wide green belt of Local broad leaf species shall be developed in the 1.628 ha land. Central Pollution Control Board guidelines shall be followed in planning and developing green belt and selection of species etc.	
21	Plantation shall be completed within first year. In case project proponent fails to carry out plantation, this environment clearance may be cancelled.	Agreed, adequate wide green belt of Local broad leaf species has been developed in the 1.764 ha land (Copy plantation report is enclosed as **Annexure -II).**
22	Project authority shall provide garland drains with appropriate check dams all along the raw materials storage areas etc. to avoid any possibility of erosion (wearing away) during rain. Sedimentation pits shall be constructed at the corners of the garland drains. Project authority shall provide adequate collection and treatment arrangement for proper management of storm water. The surface run-off shall be de-silted through a series of check dams and drains.	Well drainage system already developed in raw material storage area and other areas of the plant.
23	Project authority shall develop rainwater-harvesting structures to harvest the rainwater for utilization in the lean season as well as to recharge the ground water table. A detailed scheme for rainwater harvesting to recharge the ground water aquifer shall be prepared in consultation with Central Ground Water Authority / State Ground Water Board. A copy of the same shall be submitted within three months to the Chhattisgarh Environment Conservation Board, Raipur, Regional Office, Chhattisgarh Environment Conservation Board, Raipur, SEIAA, Chhattisgarh and Regional Office, Ministry of Environment, Forest and Climate Change, Government of India, Nagpur.	12 nos. of recharge wells and 04 nos. of ground water recharge measures have already been constructed within plant premises to recharge ground water. We have also installed ground water level recorder for measurement of ground water level. **(Photographs enclosed as Annexure - III).**
24	Occupational Health Surveillance of the workers should be done on a regular basis and records maintained as per the factories Act.	Being implemented as per Factories Act.
25	The project proponent shall also comply with all the environmental protection measures and safe	All environmental protection measures are being implemented as per the

	guards recommended in the Environment Impact Assessment Report / Environment Management Plan.	recommendations of EIA/EMP report.
26	Project authority shall establish an environmental management cell to carryout function relating to environmental management under the supervision of senior executive who shall directly report to the head of organization. A full-fledged laboratory with qualified technical / scientific staffs to monitor the influent, effluent, ground water, surface water, soil, stack emission and ambient air quality etc. shall be provided.	The Environmental Cell is functioning under well qualified environmental team of our parent company Godawari Power & Ispat Ltd. to monitor the environmental measures.
27	Adequate funds shall be allocated for undertaking CSR activities (apart from committed plantation) as per Government norms. Project authority must undertake socio-economic development activities in the surrounding villages like community development programmes, educational programmes, drinking water supply and health care etc. Details of activities shall also be submitted to Chhattisgarh Environment Conservation Board, Naya Raipur, Regional Office, Chhattisgarh Environment Conservation Board, Bilaspur SEIAA, Chhattisgarh and Regional Office, Ministry of Environment, Forest and Climate Change, Government of India, Nagpur. The funds earmarked for the environment protection measures shall not be diverted for other purpose and year-wise expenditure should be reported to the Chhattisgarh Environment Conservation Board, Naya Raipur, Regional Office, Chhattisgarh Environment Conservation Board, Bilaspur, SEIAA, Chhattisgarh and Regional Office, Ministry of Environment, Forest and Climate Change, Government of India, Nagpur.	Being complied, since the company was amalgamated with its parent company Godawari Power &Ispat Ltd., all the CSR activities done by Godawari Power & Ispat Limited are combined. Details of CSR expenditure is attached as **Annexure-IV.**
28	The issuance of this environmental clearance does not convey any property rights in either real or personal property, or any exclusive privileges, nor does not authorize any injury to	Noted and agreed.

	private property or any invasion of personal rights, nor any infringement of Central, State or Local laws or regulations.	
29	SEIAA, Chhattisgarh reserves the right to revoke the clearance if conditions stipulated are not implemented to the satisfaction. SEIAA, Chhattisgarh reserves the right to amend / cancel any of the conditions and add new conditions and make further stringent the emission / effluent limit as and when deemed necessary in the interest of environmental protection, change in the project profile or non-satisfactory implementation of the stipulated conditions etc.	Noted and agreed.
30	Local persons shall be given employment during construction (if any) and operation of the plant.	Agreed and being implemented.
31	The Project authority shall advertise in at least two local newspapers widely circulated in the region around the project, one of which shall be in the vernacular language of the locality concerned within seven days from the date of this clearance letter, informing that the project has been accorded environmental clearance and copies of clearance letter are available with the Chhattisgarh Environment Conservation Board and may also seen at Website of the Ministry of Environment, Forest and Climate Change at www.envfor.nic.in and website of SEIAA, Chhattisgarh at www.seiaacg.org.	Complied.
32	Half yearly report on the status of implementation of the stipulated conditions and environment safeguards shall be submitted to the Chhattisgarh Environment Conservation Board, Raipur, Regional Office, Chhattisgarh Environment Conservation Board, Raipur, SEIAA, Chhattisgarh and Regional Office, Ministry of Environment, Forest and Climate Change, Government of India, Nagpur.	Six monthly EC compliance status report is being submitted regularly to RO, CECB, Raipur, SEIAA, RO-Ministry of Environment, Forest and Climate change, Government of India, Nagpur.
33	Regional Office of the Ministry of Environment, Forest and Climate Change at Nagpur shall monitor the implementation of the stipulated conditions. A complete set of documents including Environment Impact Assessment	Noted and agreed.

	Report and Environment Management Plan along with the additional information submitted from time to time shall be forwarded to the Regional Office for their use during monitoring.	
34	The project authorities shall inform the Regional Office as well as the SEIAA, Chhattisgarh regarding the date of start of commissioning of plant with expanded capacity.	Complied.
35	Full cooperation shall be extended to the Scientists / Officers from the SEIAA, Chhattisgarh, Ministry of Environment, Forest and Climate Change, Government of India / Regional Office, Ministry of Environment, Forest and Climate Change, Government of India, Bhopal / the CPCB / the Chhattisgarh Environment Conservation Board, who would be monitoring the compliance of environment status.	Noted and agreed.
36	Concealing factual data or submission of false / fabricated data and failure to comply with any of the conditions mentioned above may result in withdrawal of this clearance and attract action under the provisions of the Environment (Protection) Act, 1986.	Noted
37	In case of any deviation or alteration in the expansion project from those submitted to this SEIAA, Chhattisgarh for clearance, a fresh reference should be made to the SEIAA, Chhattisgarh to assess the adequacy of the condition(s) imposed and to add additional environment protection measures required, if any. No further expansion or modifications in the plant should be carried out without prior approval of the Ministry of Environment, Forest and Climate Change, Government of India / SEIAA, Chhattisgarh.	Noted and agreed.
38	The project authorities must strictly adhere to the stipulations made by the Chhattisgarh Environment Conservation Board (CECB) and the State Government.	Noted and agreed.
39	The above stipulations would be enforced among others under the Water (Prevention and	Noted and agreed.

	Control of Pollution) Act, 1974, the Air (Prevention and Control of Pollution) Act, 1981, the Environment (Protection) act, 1986 and rules there under, Hazardous and Other Wastes (Management and Transboundary Movement) Rules, 2016 and its amendments, the Public Liability Insurance Act, 1991 and its amendments.	
40	The above conditions would be enforced inter-alia, under the provisions of the water (Prevention & Control of Pollution) Act. 1974, the Air (Prevention & Control of Pollution) Act. 1981 the environment (Protection) Act. 1986 and the public liability insurance Act, 1991 along with their amendments and Rules. The proponent shall ensure to provide for the costs incurred for taking up remedial measures in case of soil contamination, contamination of groundwater and surface water, and occupational and other diseases due to the mining operations.	Noted and agreed.
41	Chhattisgarh Environment Conservation Board shall display a copy of the clearance letter at the Regional Office, District Trade and Industries Centre and Collector's Office / Tehsildar's Office for 30 days.	Noted.
42	Any appeal against this environmental clearance shall lie with the National Green Tribunal, if preferred, within a period of 30 days as prescribed under section 16 of the National Green Tribunal Act, 2010.	Noted and agreed.

SUPPORTING DOCUMENTS INCLUDE AS ANNEXURES

ANNEXURE - I

Audiometry Test Reports-2021

S.NO.	Emp. Code	Name	Designation	Right Ear	Left Ear	Status
1	103249	AJAY YADAV	FITTER/RIGGER	20.42	20.28	Normal
2	104006	ANAND RAM SAHU	TURNER	22.85	23.42	Normal
3	103301	ATUL SAHU	D.E.T.	21.28	21.57	Normal
4	103175	AWADH SHARAN PANDEY	ASST MANAGER QUALITY	18.71	20.57	Normal
5	120006	AWADHESH MAHTO	SHIFT INCHARGE	23.42	23.71	Normal
6	103233	BHUSHAN LAL SAHU	SR. FITTER	18	18.85	Normal
7	109002	BUDHE LAL VERMA	ASST MANAGER GASIFIRE	19	17.71	Normal
8	107001	CH. DHARMA RAO	ASST MANAGER RAW MATERIAL	22.28	22.57	Normal
9	103205	CHAMMAN LAL MARKANDE	FITTER	20.85	20.57	Normal
10	103070	DEVANANDA PRADHAN	FOLLER OPERATOR	21.71	21.42	Normal
11	000586	DINESH KUMAR VERMA	Hydra oprt	18.71	19	Normal
12	103120	DURGA PRASAD SAHU	Hydra oprt	18.71	18.28	Normal
13	103061	GOPAL VISHWKARMA	Turner	22.57	22.14	Normal
14	103277	Gyan Das Manikpuri	DIE MAKER	20.71	22.57	Normal
15	103278	HIRA LAL AJAD	FITTER	21	20.85	Normal

JUPITER HEALTH CARE

AMRIT SANDESH BUILDING SHASTRI CHOWK RAIPUR C.G.

COMPANY : R.R. ISPAT

REF. BY :

R.D. NO. : 999

NAME : AJAY YADAV

AGE : 46/M

DATE : 17-03-2021

AUDIOGRAM

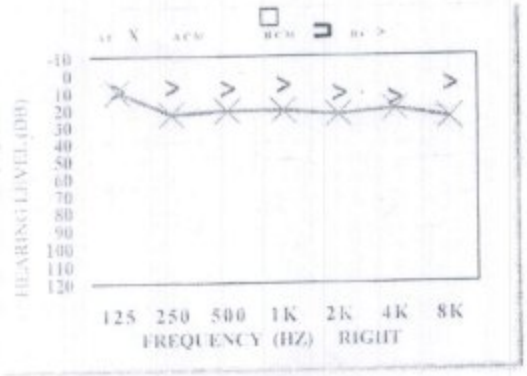

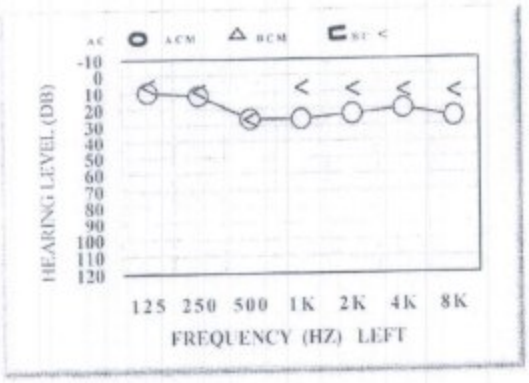

MODE / EAR	AIR CONDUCTION		BONE CONDUCTION		COLOUR CODE	THRESHHOLD IN dB	RIGHT	LEFT
	MASKED	UNMASKED	MASKED	UNMASKED		AIR CONDUCTION	20.428571	20.285714
LEFT	□	×	⊐	>	BLUE	BONE CONDUCTION		
RIGHT	△	○	⊏	<	RED	SPEECH		

NO RESPONSE : ADD ↓BELOW THE RESPECTIVE SYMBOLS

REMARK : NORMAL HEARING IN BOTH EARS

G.A

Dr. Gaurav Ahluwalia
MBBS,DNB (ENT), FRCSI
Fellowship in FESS,ACLS
Reg. No. - CGMC 2228/2009

JUPITER HEALTH CARE

AMRIT SANDESH BUILDING SHASTRI CHOWK RAIPUR C.G.

COMPANY : R.R ISPAT

R.D. NO. : 64

NAME : ANAND RAM SAHU

AGE : 53/M

DATE : 16-03-2021

AUDIOGRAM

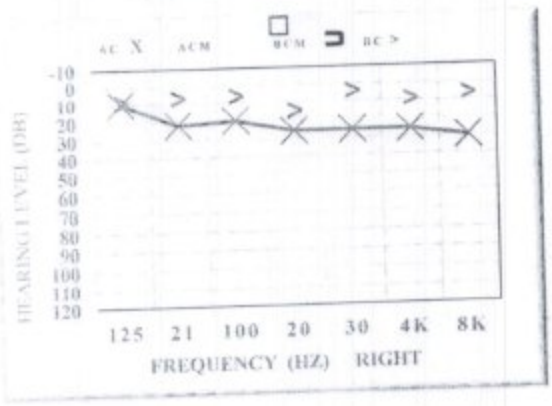

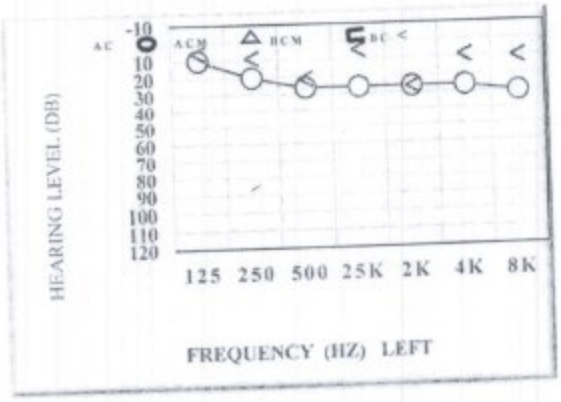

MODE / EAR	AIR CONDUCTION		BONE CONDUCTION		COLOUR CODE	THRESHHOLD IN dB	RIGHT	LEFT
	MASKED	UNMASKED	MASKED	UNMASKED		AIR CONDUCTION	22.857143	23.428571
LEFT	□	×	⊐	>	BLUE	BONE CONDUCTION		
RIGHT	△	○	⊂	<	RED	SPEECH		

NO RESPONSE : ADD ↓BELOW THE RESPECTIVE SYMBOLS

REMARK : NORMAL HEARING IN BOTH EARS

Dr. Gaurav Anluwalia
MS
Reg. No. - GMC / 3/2009

JUPITER HEALTH CARE

AMRIT SANDESH BUILDING SHASTRI CHOWK RAIPUR C.G.

COMPANY : R.R ISPAT

R.D. NO. : 44

NAME : ATUL SAHU

AGE : 23/M

DATE : 17-03-2021

AUDIOGRAM

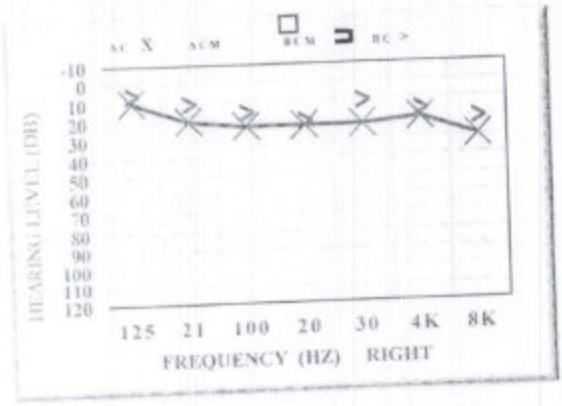

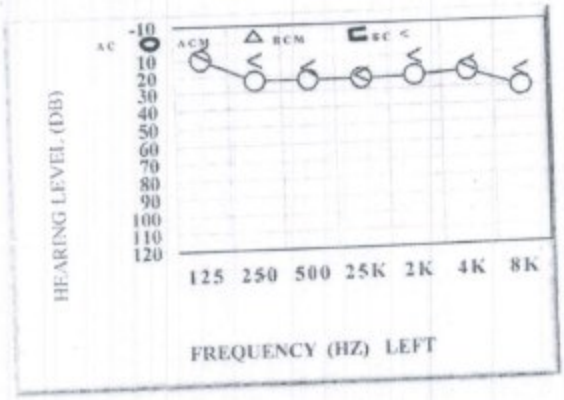

MODE / EAR	AIR CONDUCTION		BONE CONDUCTION		COLOUR CODE	THRESHHOLD IN dB	RIGHT	LEFT
	MASKED	UNMASKED	MASKED	UNMASKED		AIR CONDUCTION	21.285714	21.571429
LEFT	□	×	⊐	>	BLUE	BONE CONDUCTION		
RIGHT	△	○	⊏	<	RED	SPEECH		

NO RESPONSE : ADD ↓BELOW THE RESPECTIVE SYMBOLS

REMARK : NORMAL HEARING IN BOTH EARS

Dr. Gaurav Ahluwalia

JUPITER HEALTH CARE

AMRIT SANDESH BUILDING SHASTRI CHOWK RAIPUR C.G.

COMPANY : R.R ISPAT

REF. BY :

R.D. NO. : 563

NAME : AWADH SHARAN PANDEY

AGE : 51/M

DATE : 18-03-2021

AUDIOGRAM





MODE / EAR	AIR CONDUCTION		BONE CONDUCTION		COLOUR CODE	THRESHHOLD IN dB	RIGHT	LEFT
	MASKED	UNMASKED	MASKED	UNMASKED		AIR CONDUCTION	18.714286	20.571429
LEFT	□	×	⊐	>	BLUE	BONE CONDUCTION		
RIGHT	△	○	⊏	<	RED	SPEECH		

NO RESPONSE : ADD ↓BELOW THE RESPECTIVE SYMBOLS

REMARK : NORMAL HEARING IN BOTH EARS

G.A

Dr. Gaurav Ahluwalia
MBBS,DNB (ENT), FRCSI
Fellowship in FESS,ACLS
Reg. No. - CGMC 2228/2009

JUPITER HEALTH CARE

AMRIT SANDESH BUILDING SHASTRI CHOWK RAIPUR C.G.

COMPANY : R.R ISPAT

R.D. NO. : 33

NAME : AWADHISH MAHLO

AGE : 46/M

DATE : 18-03-2021

AUDIOGRAM

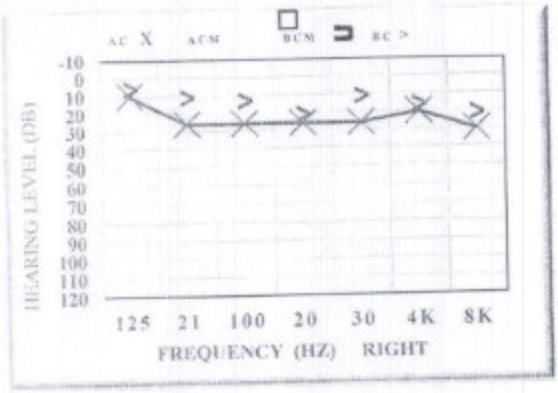

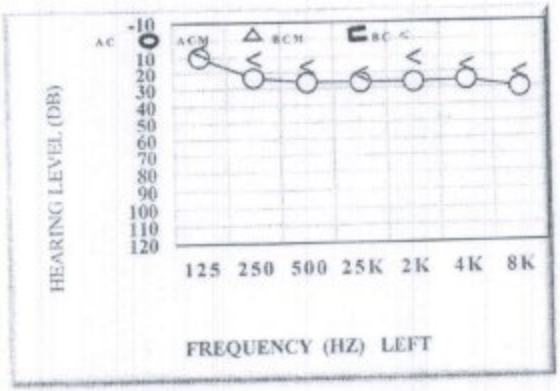

MODE / EAR	AIR CONDUCTION MASKED	AIR CONDUCTION UNMASKED	BONE CONDUCTION MASKED	BONE CONDUCTION UNMASKED	COLOUR CODE
LEFT	□	×	⊃	>	BLUE
RIGHT	△	○	⊂	<	RED

NO RESPONSE : ADD ↓BELOW THE RESPECTIVE SYMBOLS

THRESHHOLD IN dB	RIGHT	LEFT
AIR CONDUCTION	23.428571	23.714286
BONE CONDUCTION		
SPEECH		

REMARK : NORMAL HEARING IN BOTH EARS

G.A.

Dr. Gaurav Agrawal
MBBS, MD (Gen. Med.)
Consultant Physician
Reg. No. - CGMC 2238/2009

JUPITER HEALTH CARE

AMRIT SANDESH BUILDING SHASTRI CHOWK RAIPUR C.G.

COMPANY : R.R ISPAT

REF. BY :

R.D. NO. : 565

NAME : BHUSHAN LAL SAHU

AGE : 45/M

DATE : 19-03-2021

AUDIOGRAM

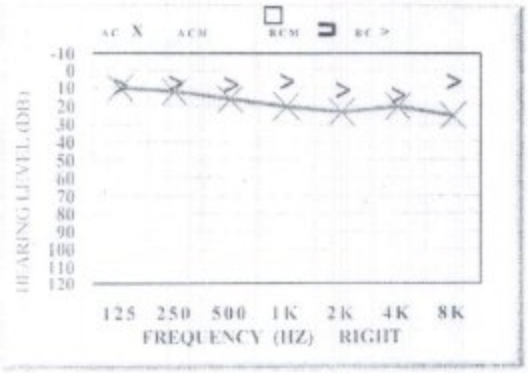



MODE / EAR	AIR CONDUCTION		BONE CONDUCTION		COLOUR CODE	THRESHHOLD IN dB	RIGHT	LEFT
	MASKED	UNMASKED	MASKED	UNMASKED		AIR CONDUCTION	18	18.857143
LEFT	□	×	⊐	>	BLUE	BONE CONDUCTION		
RIGHT	△	○	⊏	<	RED	SPEECH		

NO RESPONSE : ADD ↓BELOW THE RESPECTIVE SYMBOLS

REMARK : NORMAL HEARING IN BOTH EARS

G.A

Dr. Gaurav Ahluwalia
MBBS,DNB (ENT), FRCSI
Fellowship in FESS,ACLS
Reg. No. - CGMC 2228/2009

JUPITER HEALTH CARE

AMRIT SANDESH BUILDING G.E. ROAD RAIPUR C.G.

DR	R.R ISPAT	REF. BY :
R.D. NO. :	231	
NAME	BUDHELAL VERMA	
AGE :	51/M	
DATE :	18-03-2021	

AUDIOGRAM





MODE / EAR	AIR CONDUCTION MASKED	AIR CONDUCTION UNMASKED	BONE CONDUCTION MASKED	BONE CONDUCTION UNMASKED
LEFT	□	[illegible]	[illegible]	>
RIGHT	△	[illegible]	[illegible]	<

NO RESPONSE : ADD ↓BELOW THE RESPECTIVE SYMBOLS

COLOUR CODE	THRESHHOLD IN dB	RIGHT	LEFT
	AIR CONDUCTION	19	17.714
BLUE	BONE CONDUCTION		
RED	SPEECH		

REMARK : NORMAL HEARING IN BOTH EARS

G.A

Dr. Gaurav Ahluwalia
MBBS,DNB (ENT), FRCSI
Fellowship in FESS,ACLS
Reg. No. - CGMC 2228/2009

JUPITER HEALTH CARE

AMRIT SANDESH BUILDING SHASTRI CHOWK RAIPUR C.G.

COMPANY : R.R ISPAT

R.D. NO. : 53

NAME : CH.DHARMA RAO

AGE : 49/M

DATE : 16-03-2021

AUDIOGRAM





MODE / EAR	AIR CONDUCTION		BONE CONDUCTION		COLOUR CODE	THRESHHOLD IN dB		RIGHT	LEFT
	MASKED	UNMASKED	MASKED	UNMASKED		AIR CONDUCTION		22.285714	22.571429
LEFT	□	×	⊃	>	BLUE	BONE CONDUCTION			
RIGHT	△	○	⊂	<	RED	SPEECH			

NO RESPONSE : ADD ↓BELOW THE RESPECTIVE SYMBOLS

REMARK : NORMAL HEARING IN BOTH EARS

Dr. Gaurav Ahluwalia
SI
S
Reg. No. - GMC 2[illegible]8/2009

JUPITER HEALTH CARE

AMRIT SANDESH BUILDING G.E. ROAD RAIPUR C.G.

DR	R.R. ISPAT	REF. BY :
R.D. NO. :	302	
NAME	CHAMMAN LAL MARKANDE	
AGE :	33/M	
DATE :	17-03-2021	

AUDIOGRAM



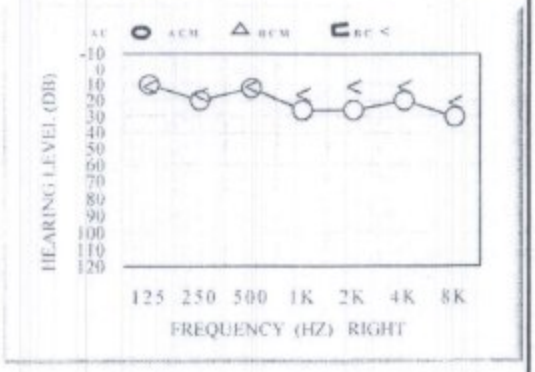

MODE / EAR	AIR CONDUCTION		BONE CONDUCTION		COLOUR CODE	THRESHHOLD IN dB		RIGHT	LEFT
	MASKED	UNMASKED	MASKED	UNMASKED		AIR CONDUCTION		20.857143	20.571
LEFT	□	×	⊐	>	BLUE	BONE CONDUCTION			
RIGHT	△	○	⊏	<	RED	SPEECH			

NO RESPONSE : ADD ↓BELOW THE RESPECTIVE SYMBOLS

REMARK : NORMAL HEARING IN BOTH EARS

G.A

Dr. Gaurav Ahluwalia
MBBS,DNB (ENT), FRCSI
Fellowship in FESS,ACLS
Reg. No. - CGMC 2228/2009

JUPITER HEALTH CARE

AMRIT SANDESH BUILDING SHASTRI CHOWK RAIPUR C.G.

COMPANY : R.R ISPAT

R.D. NO. : 46

NAME : DEVANAND PRADHAN

AGE : 33/M

DATE : 17-03-2021

AUDIOGRAM





MODE / EAR	AIR CONDUCTION		BONE CONDUCTION		COLOUR CODE	THRESHHOLD IN dB		RIGHT	LEFT
	MASKED	UNMASKED	MASKED	UNMASKED		AIR CONDUCTION		21.714286	21.428571
LEFT	□	×	⊐	>	BLUE	BONE CONDUCTION			
RIGHT	△	○	⊏	<	RED	SPEECH			

NO RESPONSE : ADD ↓BELOW THE RESPECTIVE SYMBOLS

REMARK : NORMAL HEARING IN BOTH EARS

Dr. Gaurav Ahluwalia

O+ve
Group missing

JUPITER HEALTH CARE

AMRIT SANDESH BUILDING SHASTRI CHOWK RAIPUR C.G.

COMPANY : R.R. ISPAT

REF. BY :

R.D. NO. : 405

NAME : DINESH KUMAR VERMA

AGE : 32/M

DATE : 16-03-2021

AUDIOGRAM



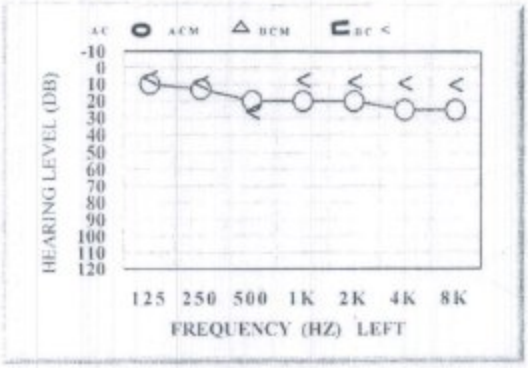

MODE / EAR	AIR CONDUCTION		BONE CONDUCTION		COLOUR CODE	THRESHHOLD IN dB	RIGHT	LEFT
	MASKED	UNMASKED	MASKED	UNMASKED		AIR CONDUCTION	18.714286	19
LEFT	□	×	⊐	>	BLUE	BONE CONDUCTION		
RIGHT	△	○	⊏	<	RED	SPEECH		

NO RESPONSE : ADD ↓BELOW THE RESPECTIVE SYMBOLS

REMARK : NORMAL HEARING IN BOTH EARS

G.A

Dr. Gaurav Ahluwalia
MBBS,DNB (ENT), FRCSI
Fellowship in FESS,ACLS
Reg. No. - CGMC 2228/2009

JUPITER HEALTH CARE

AMRIT SANDESH BUILDING SHASTRI CHOWK RAIPUR C.G.

COMPANY : R.R. ISPAT

REF. BY :

R.D. NO. : 801

NAME : DURGA PRASAD SAHU

AGE : 36/M

DATE : 17-03-2021

AUDIOGRAM





MODE / EAR	AIR CONDUCTION		BONE CONDUCTION		COLOUR CODE	THRESHHOLD IN dB		RIGHT	LEFT
	MASKED	UNMASKED	MASKED	UNMASKED		AIR CONDUCTION		18.714286	18.285714
LEFT	□	×	⊐	>	BLUE	BONE CONDUCTION			
RIGHT	△	○	⊏	<	RED	SPEECH			

NO RESPONSE : ADD ↓BELOW THE RESPECTIVE SYMBOLS

REMARK : NORMAL HEARING IN BOTH EARS

GA.

Dr. Gaurav Ahluwalia
MBBS,DNB (ENT), FRCSI
Fellowship in FESS,ACLS
Reg. No. - CGMC 2228/2009

JUPITER HEALTH CARE

AMRIT SANDESH BUILDING SHASTRI CHOWK RAIPUR C.G.

COMPANY : R.R ISPAT

R.D. NO. : 90

NAME : GOPAL VISHWAKARMA

AGE : 50/M

DATE : 17-03-2021

AUDIOGRAM

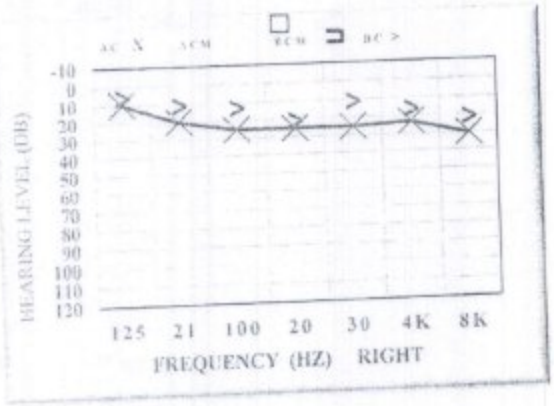

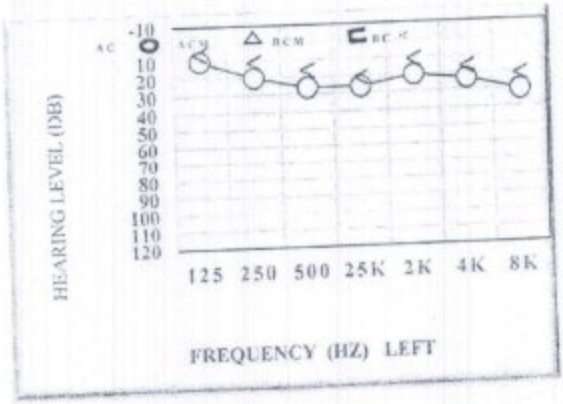

MODE / EAR	AIR CONDUCTION MASKED	AIR CONDUCTION UNMASKED	BONE CONDUCTION MASKED	BONE CONDUCTION UNMASKED	COLOUR CODE
LEFT	□	×	⊐	>	BLUE
RIGHT	△	○	⊏	<	RED

NO RESPONSE : ADD ↓BELOW THE RESPECTIVE SYMBOLS

THRESHHOLD IN dB	RIGHT	LEFT
AIR CONDUCTION	22.571429	22.142857
BONE CONDUCTION		
SPEECH		

REMARK : NORMAL HEARING IN BOTH EARS

Dr. Gaurav Ahluwalia

JUPITER HEALTH CARE

AMRIT SANDESH BUILDING SHASTRI CHOWK RAIPUR C.G.

COMPANY : R.R ISPAT

REF. BY :

R.D. NO. : 628

NAME : GYAN DAS MANIKPURI

AGE : 30/M

DATE : 18-03-2021

AUDIOGRAM



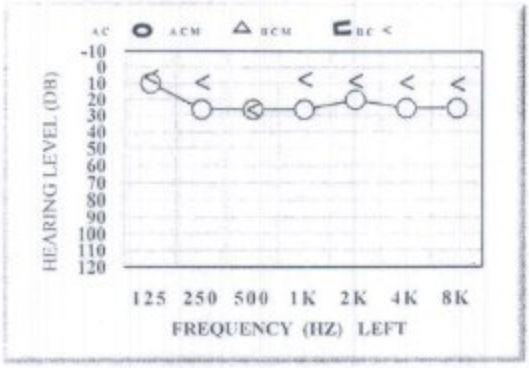

MODE / EAR	AIR CONDUCTION		BONE CONDUCTION		COLOUR CODE	THRESHHOLD IN dB		RIGHT	LEFT
	MASKED	UNMASKED	MASKED	UNMASKED		AIR CONDUCTION		20.714286	22.571429
LEFT	□	×	⊐	>	BLUE	BONE CONDUCTION			
RIGHT	△	○	⊏	<	RED	SPEECH			

NO RESPONSE : ADD ↓BELOW THE RESPECTIVE SYMBOLS

REMARK : NORMAL HEARING IN BOTH EARS

G.A

Dr. Gaurav Ahluwalia
MBBS,DNB (ENT), FRCSI
Fellowship in FESS,ACLS
Reg. No. - CGMC 2228/2009

JUPITER HEALTH CARE

AMRIT SANDESH BUILDING SHASTRI CHOWK RAIPUR C.G.

COMPANY : R.R ISPAT

REF. BY :

R.D. NO. : 5632

NAME : HIRALAL AZAD

AGE : 31/M

DATE : 18-03-2021

AUDIOGRAM



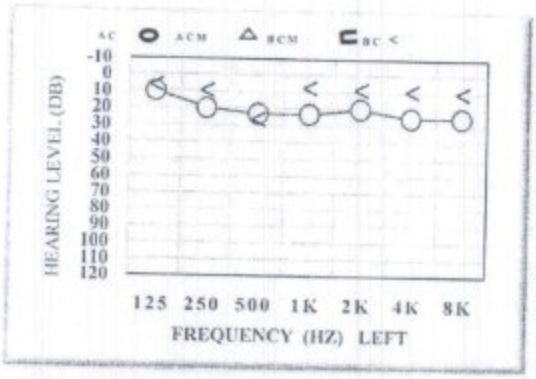

MODE / EAR	AIR CONDUCTION		BONE CONDUCTION		COLOUR CODE	THRESHHOLD IN dB	RIGHT	LEFT
	MASKED	UNMASKED	MASKED	UNMASKED		AIR CONDUCTION	21	20.857143
LEFT	□	×	⊐	>	BLUE	BONE CONDUCTION		
RIGHT	△	○	⊏	<	RED	SPEECH		

NO RESPONSE : ADD ↓BELOW THE RESPECTIVE SYMBOLS

REMARK : NORMAL HEARING IN BOTH EARS

G.A

Dr. Gaurav Ahluwalia
MBBS,DNB (ENT), FRCSI
Fellowship in FESS,ACLS
Reg. No. - CGMC 2228/2009

All dimensions are in mm

ANNEXURE – II

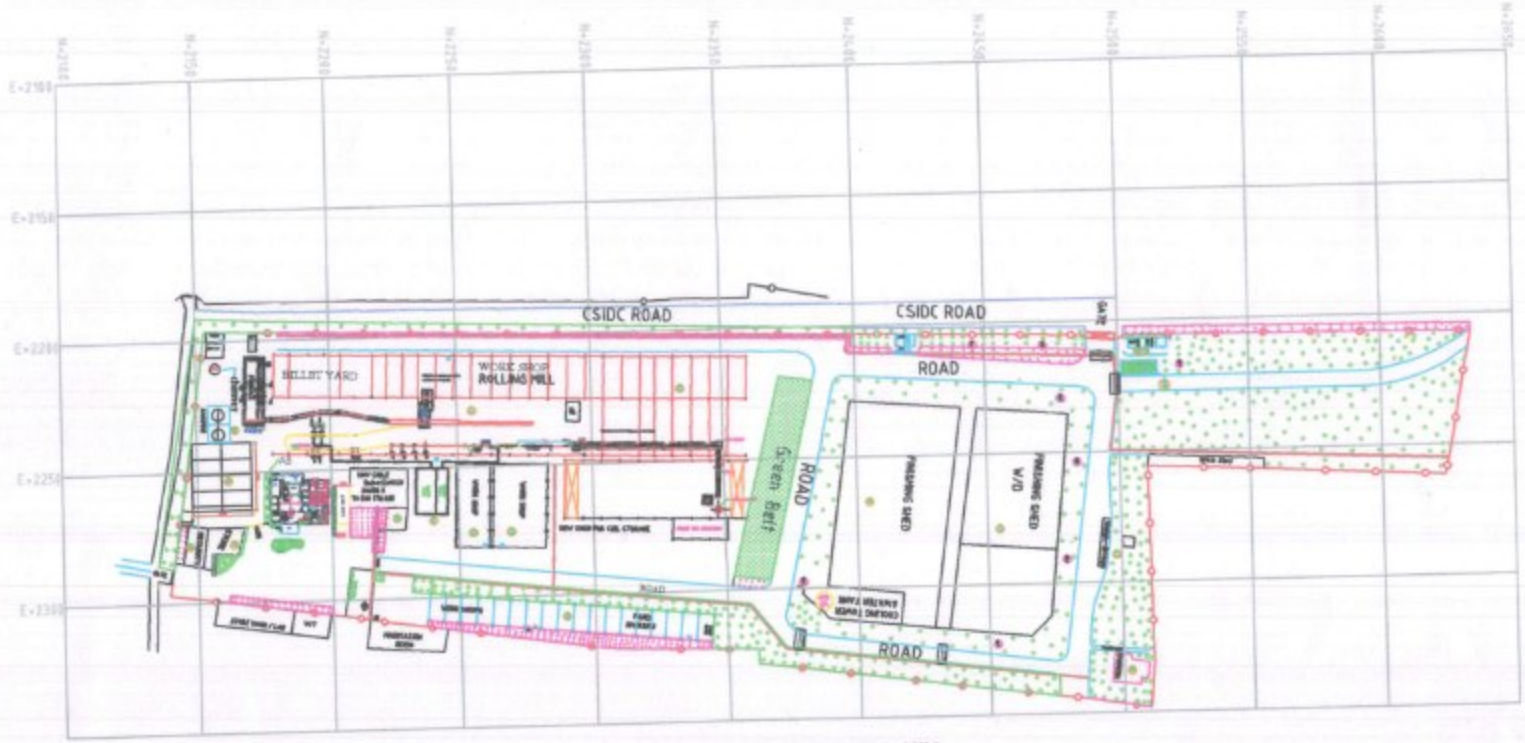

PLAN OF R.R. ISPAT ROLLING MILL

TOTAL LAND AREA 5.348 HEC.
GREEN BELT 33% OF THE TOTAL LAND 1.764 HE

LAND USED DETAIL

S.NO	DESCRIPTION	AREA IN HA	AREA IN SQM	AREA IN
1	AREA FOR EXISTING ROLLING MILL, INCLUDING CHIMNEY, GANTRIES, FURNACE, MILL STORES	0.831	8310	0.0
2	AREA FOR T/O	0.547	5470	1.0
3	COOLING AREA & STOCK YARD	1.418	14180	0.4
4	GREEN BELT AREA	1.764	17640	0.3
5	ROAD AND OPEN AREA	0.80	8000	1.7
	TOTAL LAND AREA	5.348 HEC.	53480 SQM.	15.0

Rikapal

SR.No	DESCRIPTION	REV. BY	APPD. BY
1			
2			
3			
4			

REVISIONS

THE SLAVIRA IS CONFIDENTIAL PROPERTIES OF M/S SPIAT AND ANY REPRODUCTION OR DISCLOSURE WITHOUT PERMISSION SHALL BE LIABLE FOR LEGAL ACTION.

HIRA
BUILDING STRONGER TOGETHER

R.R. ISPAT (A UNIT OF GPIL)
490/1 URLA INDUSTRIAL COMPLEX,
URLA RAIPUR (C.G.)

Drn.	S.MGARG	18.10.21
Dgn.		
Chd.	SK AGARWAL	18.10.21
Appd.	S. AGARWAL	18.10.21
Appd.		
Scale		

TITLE:-
SURFACE PLAN
R.R. ISPAT ROLL
MILL

DRG. NO. HIR/SURFACE PLAN/000

IF ANY DOUBT PLEASE ASK

Rain Water Harvesting for Shed

Rain Water Harvesting Pits / Recharge Wells

Piezo Meter

Digital Water Meter in Bore at Gate No. 3

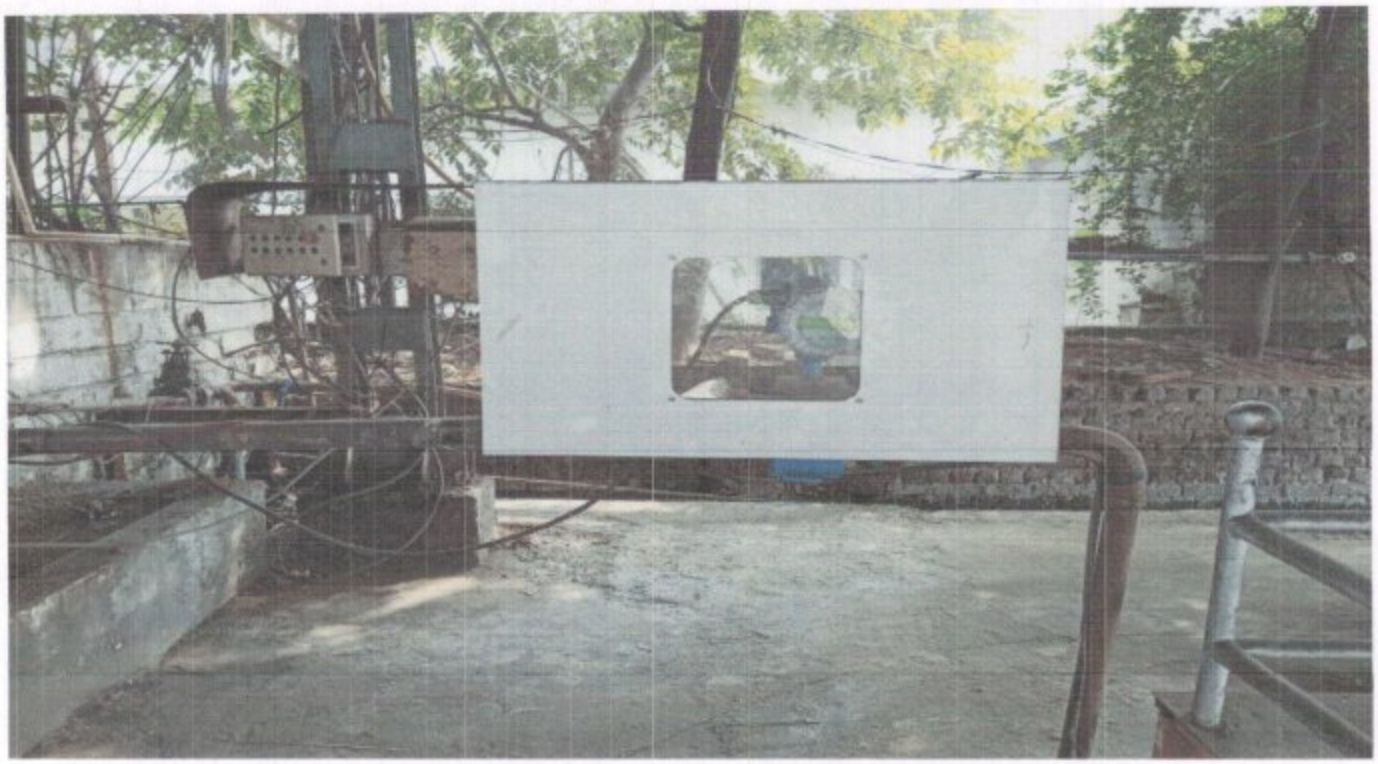

Bore with Digital Water Meter at Car Parking Area near Admn. Building

Bore with Digital Water Meter near Cooling Tower

ANNEXURE -

CSR Expenses of Godawari Power & Ispat Limited (GPIL Siltara, Kachhe Aridongri Iron Ore Mines, Boria Tibu Iron Ore Mines, HIR
City Office & R.R.Ispat) for FY: 2021-22 (Apr'21 - Sept'21)

S.No.	CSR project or activity identified.	Sector in which the Project is covered. (Environment Conservation, Infrastructure Development, Sports, Health Care, Drinking Water, Infrastructural Development & Environment, Educational Support, Environment,any other)	Projects or Programs (1) Local area or other (2) Specify the State and district where projects or programs was undertaken.	Amount spent on the projects or programs Sub-heads: (1) Direct expenditure on projects or programs. (2)Overheads: (In lac.)	Amo Dire impl agen
1	Providing Safe Drinking Water supply by Water Tankers in nearby villages during Summer	Drinking Water	Gram Panchayat Tanda, Siltara, Mandhar, Charoda, Mohadi & Dharsiwa	9.97	Dire
2	Salary paid to the 01 Community Teacher & 03 Night Guards in schools of nearby villages for promoting education	Education	Gram Panchayat Siltara, Mandhar & Tanda	0.88	Dire
3	Expenses incurred in Manpower engaged for maintenance of Plantation in Janpad Office Dharsiwa	Environment Conservation	Gram Panchayat Dharsiwa	0.40	Hort Dep
4	Financial Aid provided to Aakanksha Lions School for Mentally Handicapped Children for smooth operation of school	Education	Raipur City	12.00	Dire Aak Scho
5	Monthly Financial Aid for livelihood of 04 Girls of village Dhaneli	Livelihood	Gram Panchayat Dhaneli	0.25	Dire
6	Pond Deepening & Cleaning at Village Tanda (5.50 Acre)	Community Welfare	Gram Panchayat Tanda	19.75	Dire
7	Construction of Waiting Room & Storage Shade at Muktidhaam Mandhar	Community Welfare	Gram Panchayat Mandhar	1.54	Dire
8	Financial Contribution to Feel Parmartham Foundation for Shelter / Rehab Centre for Elderly and mentally ill abandoned people	Community Welfare	Bhilai City	0.15	Dire
9	Repairing & Leveling of roads by providing slag material & JCB for nearby villages of GPIL during monsoon season	Infrastructure Development	Gram Panchayat Tanda, Siltara, Mandhar, Neuirdih, Charoda,	2.48	Dire

Rshaped

S.No.	CSR project or activity identified.	Sector in which the Project is covered. (Environment Conservation, Infrastructure Development, Sports, Health Care, Drinking Water, Infrastructural Development & Environment, Educational Support, Environment,any other)	Projects or Programs (1) Local area or other (2) Specify the State and district where projects or programs was undertaken.	Amount spent on the projects or programs Sub-heads: (1) Direct expenditure on projects or programs. (2)Overheads: (In lac.)	Amo Direc impl agen
10	Expenses of Vermi Compost, Tractor Operator, Manpower engaged in maintenance of 102 Acre Land Green Belt Area (Oxy Zone) in Siltara	Environment Conservation	Gram Panchayat Siltara	1.52	Direc
11	Free Ambulance Services to Govt. Hospital Dharsiwa During 2nd Wave of COVID-19	COVID-19 Relief Management	Nearby Villages of GPIL	2.02	Direc
12	Financial Aid for Medical Treatment to Ms. Aakarshika Pandey (Age-21 Yrs)	Healthcare	Raipur City	5.00	Direc
13	Financial Assistance for COVID Relief to Central Postal Ladies Organization	COVID-19 Relief Management	Pan India	5.00	Direc
14	Financial Assistance for COVID Relief to Gram Panchayat Siltara	COVID-19 Relief Management	Gram Panchayat Siltara	0.50	Direc
15	Financial Aid to Hargovind Rai Ganpatrai Charitable Trust for Setup of COVID Center	COVID-19 Relief Management	Raipur City	2.00	Direc
16	Purchase & Transportation Charges of Medical Oxygen Gas for supply in Hospitals & COVID Care Centers	COVID-19 Relief Management	Raipur District, Kabirdhaam District & Kanker District	27.54	Direc
17	Financial Aid to Sumit Foundation for Ventilator Ambulance during COVID-19 Crises	COVID-19 Relief Management	Raipur City	2.00	Direc
18	Expenses on Maintenance of Garden & Plantation at Swami Vivekanada International Airport, Raipur	Environment Conservation	Raipur City	0.70	Direc Powe Ltd.
19	Maintenance of Garden & Fountain in Telibandha Chowk (Manpower, Land Escaping, Plantation Etc.)	Environment Conservation	Raipur City	2.88	Direc
20	Maintenance expenses on Plantation at RKC Compound	Environment Conservation	Raipur City	1.63	Direc
21	Procurement of Remidisiver Injection on request of CMHO through Collector Kabirdhaam	COVID-19 Relief Management	Kabirdhaam District	47.04	Direc

S.No.	CSR project or activity identified.	Sector in which the Project is covered. (Environment Conservation, Infrastructure Development, Sports, Health Care, Drinking Water, Infrastructural Development & Environment, Educational Support, Environment,any other)	Projects or Programs (1) Local area or other (2) Specify the State and district where projects or programs was undertaken.	Amount spent on the projects or programs Sub-heads: (1) Direct expenditure on projects or programs. (2)Overheads: (In lac.)	Amou Direc imple agen
22	Procurement of 300 Pcs of Pulse Oxymeter	COVID-19 Relief Management	Raipur City	2.28	Direc
23	Medical Treatment of needy person	Healthcare	Raipur City	1.00	Direc
24	Hira CSR Foundation for School Project at VIP Road, Raipur	Infrastructure Development	Raipur City	15.00	Direc
25	Expenses on Plantation in Ambleshwar	Environment Conservation	Ambleshwar	0.17	Direc
26	Expenses on Plantation in Premises of Udyog Bhavan, Raipur	Environment Conservation	Raipur City	4.43	Direc
27	Expenses on Plantation at Industrial Area Siltara Chowk	Environment Conservation	Raipur City	41.96	Direc
28	Expenses on Plantation in Urla & Birgaon area	Environment Conservation	Raipur City	27.47	By R
			TOTAL (In Lac)	**144.55**	

HIRA RAIPUR (C.G.)
